




EINSTEIN  
TELESCOPE

# ET-COMPASS

## Task 2.3 activities planning meeting

Wed. May 6 - 9:15

M. Morandin  
INFN- PD

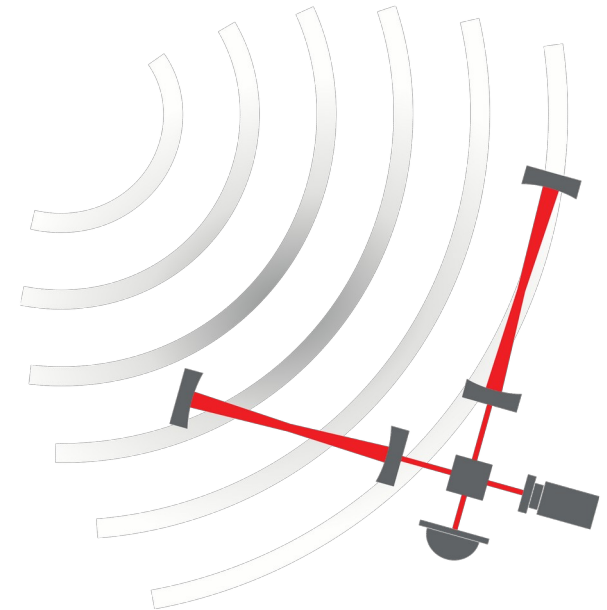

# Why this meeting (I)

- ET-COMPASS is a two years long project with 15 deliverables and 12 milestones
- to have a chance of delivering what we have pledged, it's essential
  - not to introduce dead time at the start of the project
  - to have a rapid startup-up of the activities avoiding delays that will be very difficult to recover from later in the game
- we need to make the best use of the time ahead of us this year
- risk mitigation actions include:
  - clarify ETO's plans for the activities to be carried out in 2027-8 that are relevant for the ET-COMPASS work plan
  - identify the best match between the potential that the partners can express and the needs ETO will have
    - interactions of ET-COMPASS partners with ETO are already taking place in ET-COMPASS, but in other cases they will have to be created or strengthened
  - ensure that the personnel required for the execution of the work program is going to be available when expected, especially if new hiring are planned
- this preparatory work should be done for each task

# Why this meeting (II)

- Task 2.3 is a good case to start with, since:
  - it's a complex task
  - its activities are tightly embedded in those that ETO is carrying out now and will most probably have to carry out with high priority also in the coming years
  - it's important to understand the type of contributions and resources that might be of best value for ETO
  - but also, it's important that available competences the partners can offer are exploited at best
- What comes out of the meeting today will be useful also to organize similar meetings with the other tasks.

# Agenda

- Introduction (Mauro M.) [5']
- **The ETO vision** (A. Variola) [30']:
  - General strategy for cost and risk assessments for the ET project
  - Ongoing ETO C&R assessment activities for the geometry evaluation: goals, plans, challenges
  - Scenarios for ETO C&R assessment activities in 2027-8: updated scope and tentative work plan; most effective contributions that ET-COMPASS could provide
- **Competences and resources that the ET-COMPASS partners can provide for the task 2.3 activities**
  - IFAE (M. Martinez) [5']
  - MUL (R. Galler) [5']
  - UNIRI (S. D. Jovančević) [5']
- **Roadmap for getting ready to start the task activities in ET-COMPASS** (Mario M., Alessandro V.) [20']
